


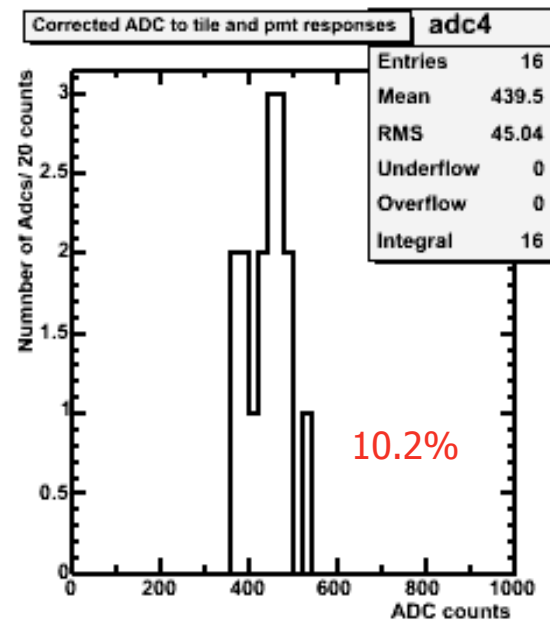
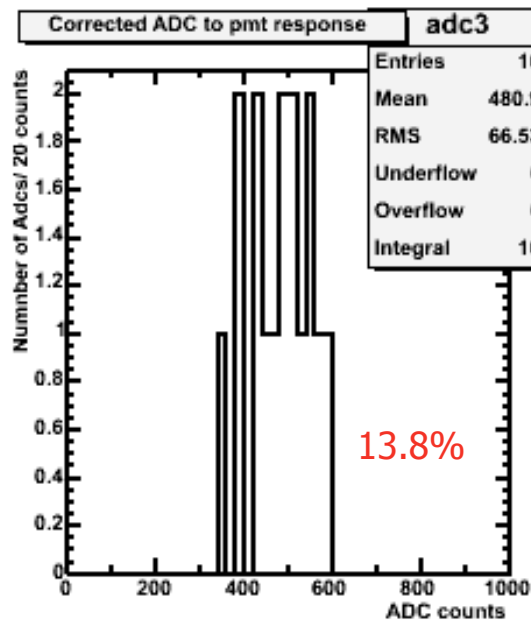
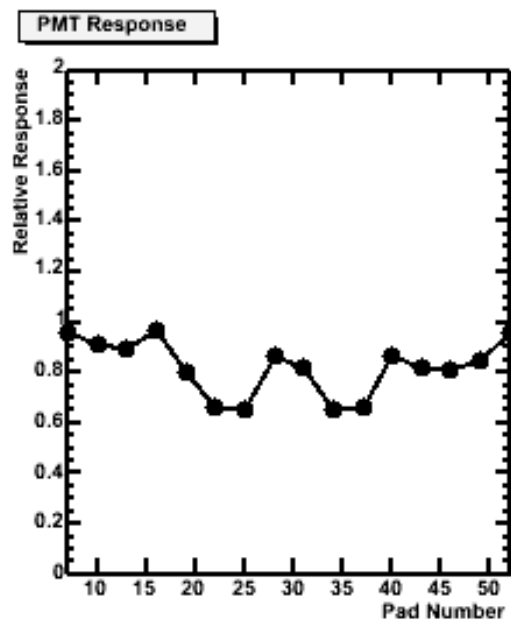


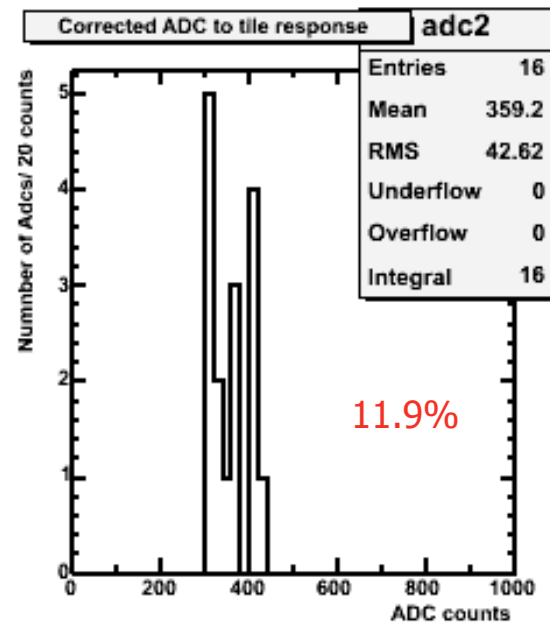



CDF Operations Summary

- Shutdown progress
 - Work continues in west and east bores
 - COT
 - Work on 1st floor cabling
 - SVX
 - Foam/RTV work done for separating SVX & COT volumes
 - Initial tests look good, but need some new sensors and further sealing work
 - CPR/CCR Run 2B upgrade continues inside SW arch
 - Aggressive schedule of an arch each two weeks (end of 1st week for SW)
 - Finishing E-M timing on SE arch
 - Finishing hadron timing level adjustment on SE arch

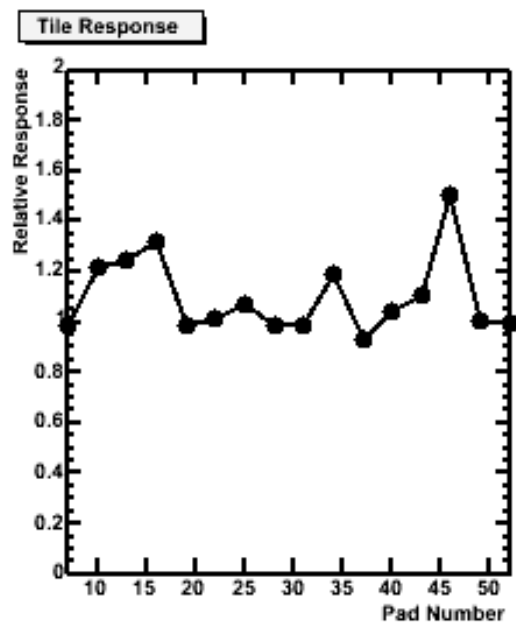

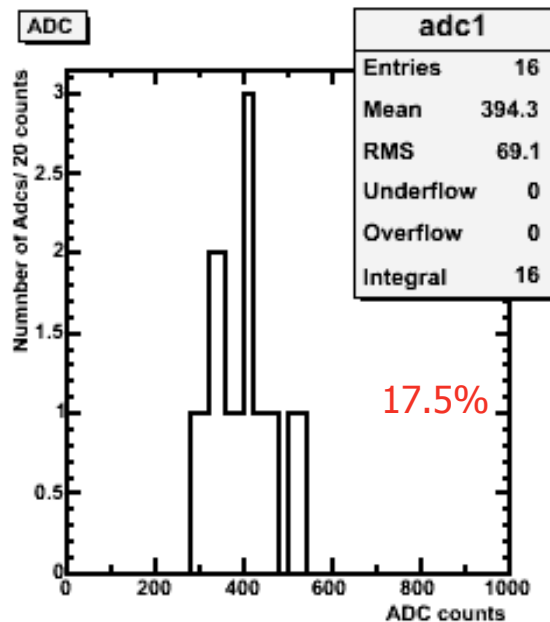

CDF Operations Summary

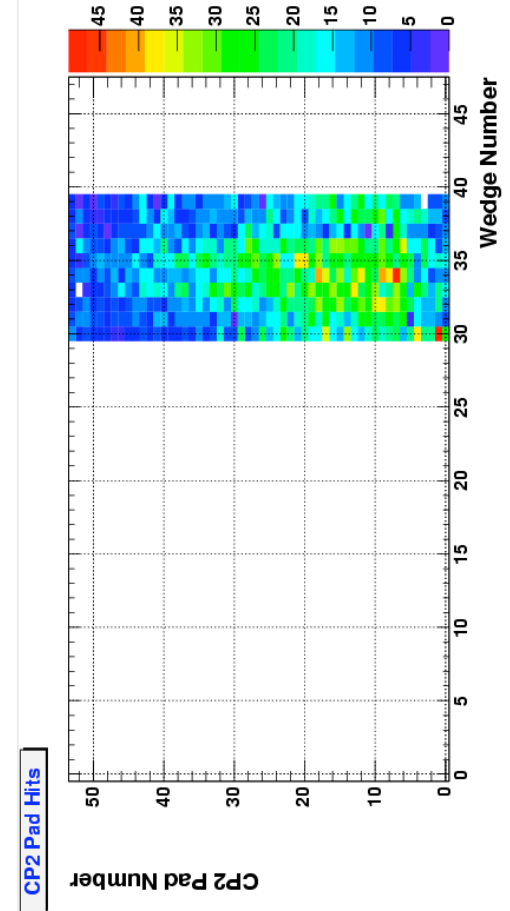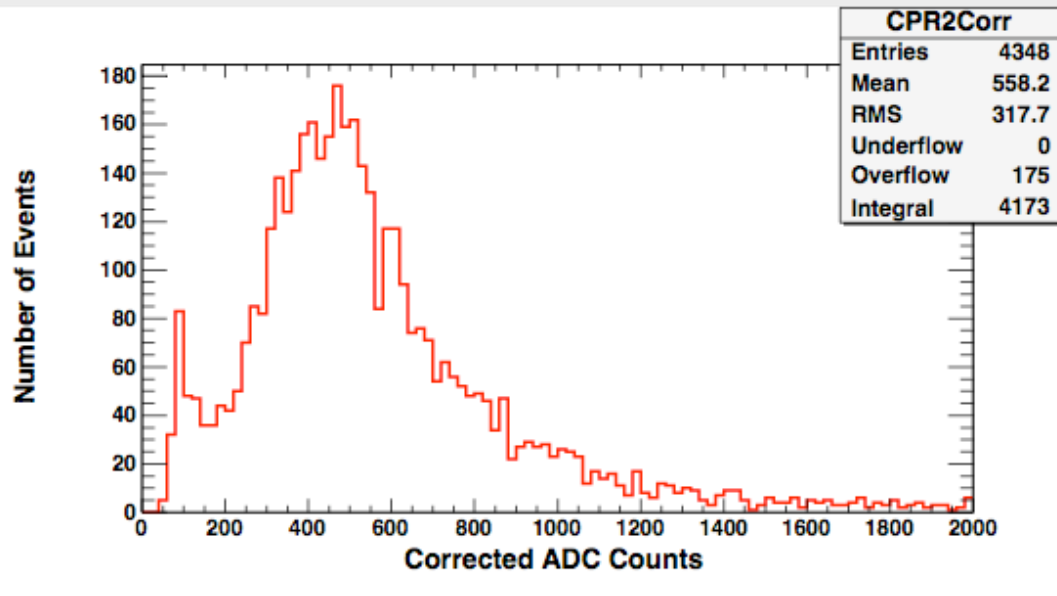



CDF Operations Summary

- Schedule
 - Recovered from three power outages; last one, last Friday
 - No DAQ today due to online fileserver expansion
 - Complete work in bores October 4 (next Monday)
 - Start flowing Ar/ethane to muon chambers
 - Cable dressing from bores till Oct. 10
 - Checkout with silicon cold and baggies Oct. 11
 - Low β quad supports installation October 18 for one week
 - Close endplugs and central arches when CCR/CPR done
 - Checkout and energize solenoid (Nov. 11)
 - Attempt tests with Ar/CO₂ in COT
